


Protect the most valuable project date with the equipment we can actually use

We identify critical equipment likely to be usable late, show which data-centre opening it will delay, and recommend whether to expedite, substitute, transfer equipment or resequence work.

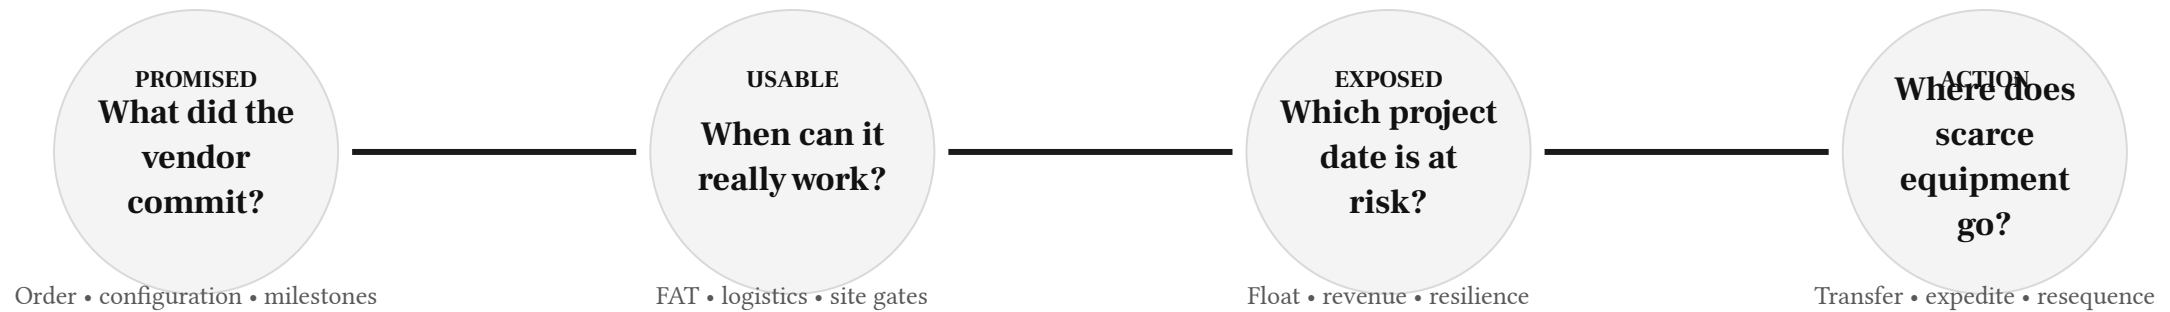


Know what was promised.

Predict what will be usable.

Move scarce equipment to where it protects the most value.

For procurement, engineering, construction and portfolio leaders deciding which threatened unit needs action—and by when.

Three projects need transformers—but the earliest opening has the least room to slip

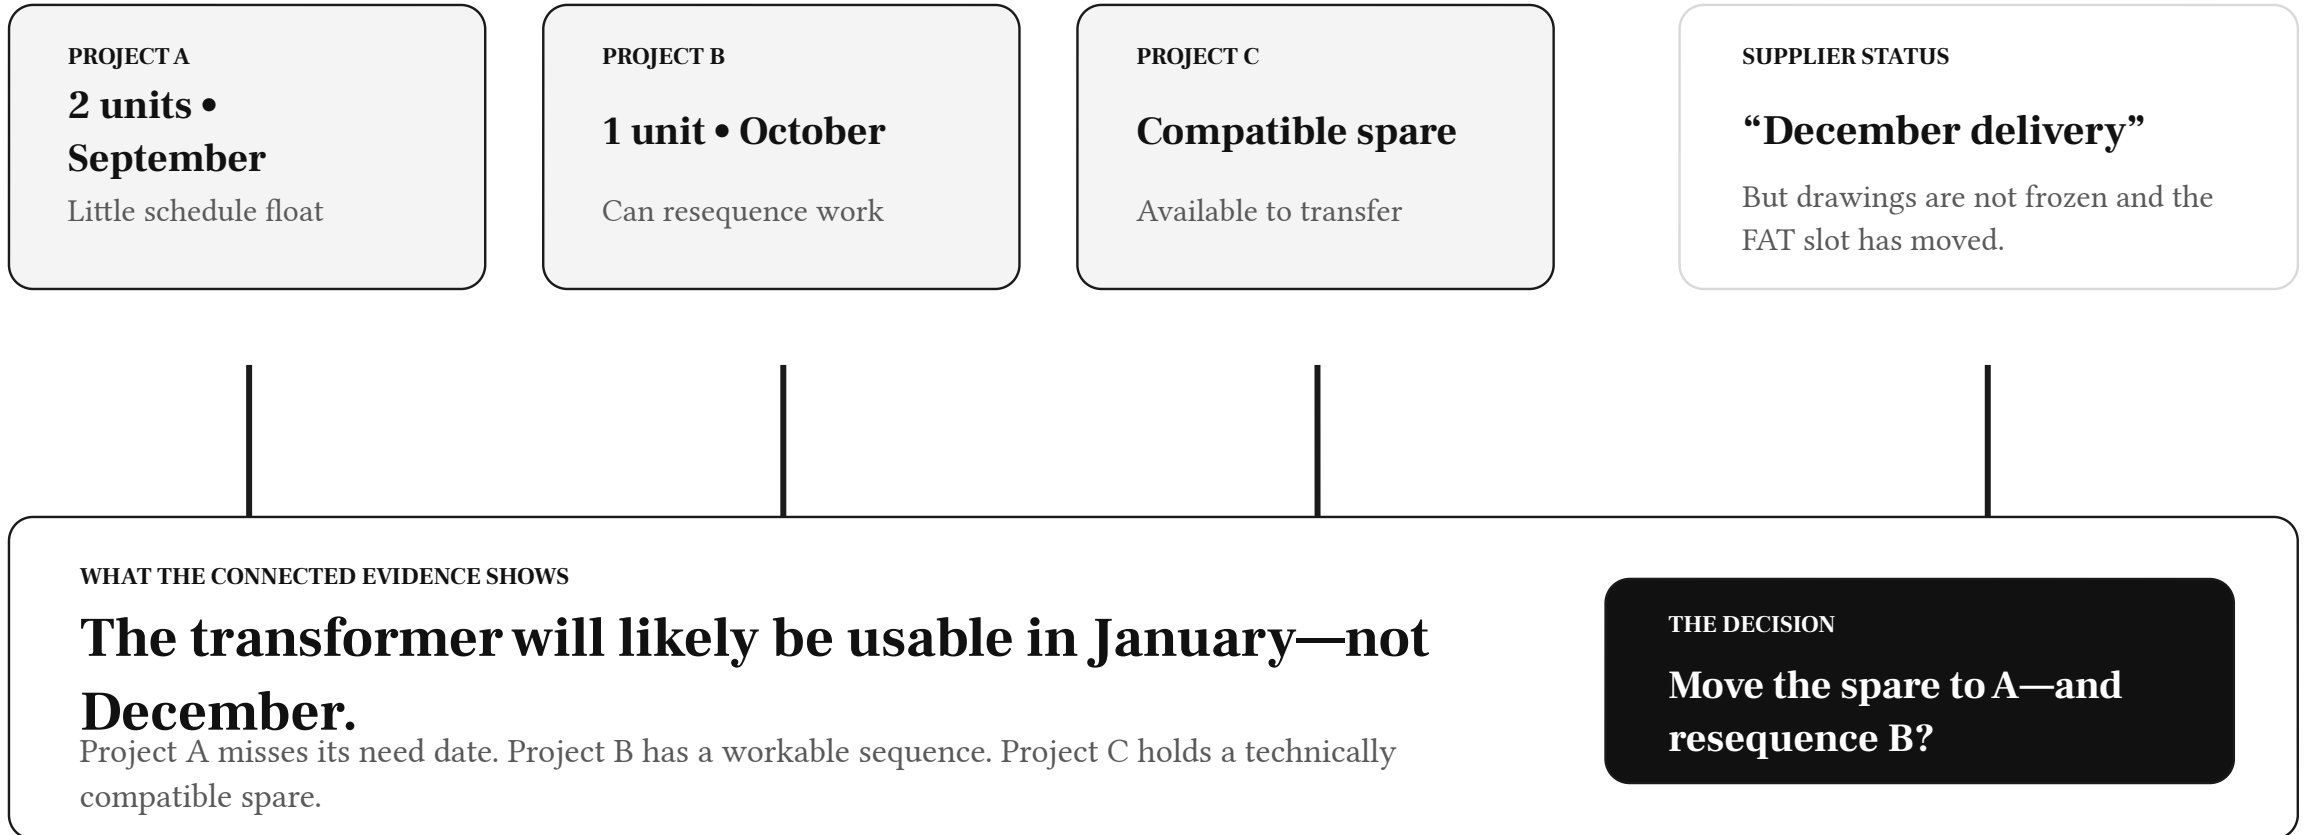

The use case becomes valuable only when it changes a portfolio action before the options close.

A decision queue—not another equipment risk register

RECOMMENDED ACTION

Transfer Transformer T-17 from Project West to Project North.

Usable-date forecast	43 days after North's need date
Limiting gates	Design approval ♦ unconfirmed FAT slot
Transfer impact	9 days of logistics; compatible configuration
Decision deadline	Procurement ♦ engineering approval by 28 Aug

WHAT THE USER CAN INSPECT

●	Unit truth	Exact model, configuration and owner
●	Readiness range	Earliest • likely • conservative
●	Project impact	Gate, float, cost and revenue
●	Feasible choices	Expedite • substitute • transfer
●	Evidence	Source, assumption and confidence

The system recommends and explains. Engineers approve equivalence; procurement and portfolio leaders approve commitments and allocation.

Turn an apparently 'on-schedule' order into an earlier, better portfolio decision

TODAY

Teams manage each order; leadership discovers the shared constraint late.

- Vendor ship date is treated as readiness
- Orders sit in separate project views
- Every late unit appears equally urgent
- Expedite is the default response
- Lessons stay in individual projects

WITH READINESS + ALLOCATION INTELLIGENCE

Every unit is connected to its usable date, project impact and feasible alternatives.

- ✓ Forecast the date the unit can be installed or energised
- ✓ See factory, component and equipment exposure across the portfolio
- ✓ Prioritise by float, revenue, cost and resilience
- ✓ Compare transfer, substitution, pooling and resequencing
- ✓ Improve vendor choice, terms and standard configurations

Practical value: earlier recovery, better use of owned spares, targeted expedite spend and fewer opening-date surprises.

Connect the order to its exact unit, readiness gates, project need and alternatives

THE DATA WE NEED

1	Order ♦ promise	POs • acknowledgements • changes
2	Exact configuration	BOM • drawings • approved alternates
3	Vendor progress	Design • production • FAT • NCRs
4	Project need	Schedule logic • float • value
5	Arrival ♦ site gates	Transport • access • foundation • install
6	Portfolio options	Inventory • location • compatibility

HOW THE ANSWER IS BUILT

- 1 Build unit-level truth**
Link order, model, factory, milestone and project
- 2 Forecast usable readiness**
Find the limiting gate and date range
- 3 Calculate project exposure**
Map delay to float, cost, revenue and latest action date
- 4 Compare feasible portfolio moves**
Rank expedite, substitute, transfer and resequence choices

Internal order, configuration and project data create the decision value. External signals sharpen timing only when mapped to the real unit, factory or route.

What must be true before we test the use case

Start with one constrained equipment class across two or three concurrent projects—not a broad supply-chain platform.

✓	A real allocation choice	At least one unit can plausibly move, substitute or change sequence
✓	Unit identity	Orders link reliably to exact configurations and projects
✓	Milestone evidence	Current and historic design, manufacture and FAT status
✓	Project consequence	Credible need dates, schedule logic, float and value assumptions
✓	Named reviewers	Procurement, engineering and project controls can validate decisions

Stop or reposition if earlier warning does not change an action, or if units cannot be tied to configurations and need dates.

Plain language on the left; technical capability on the right

WHAT THE CLIENT HEARS	WHAT WE BUILD	WHAT IT DOES
● Read orders and vendor evidence	Document intelligence	Extract configuration, dates, milestones, terms and citations
● Know which unit is which	Entity resolution	Connect model, component, factory, order, project and route
● See the real milestone history	Temporal graph	Separate reported status from evidenced completion
● Predict when it can be used	Probabilistic forecasting	Estimate readiness range, limiting gate and confidence
● Find compatible alternatives	Knowledge graph + rules	Identify candidate transfers and required adaptations
● Choose the best feasible move	Constraint optimisation	Rank actions across schedule, value and technical constraints

Control boundary: no autonomous engineering equivalence, supplier commitment, project resequencing or equipment allocation.
